




EAGLE MOUNTAIN HS





Aerial facing east highlighting the main academic building and cafeteria.

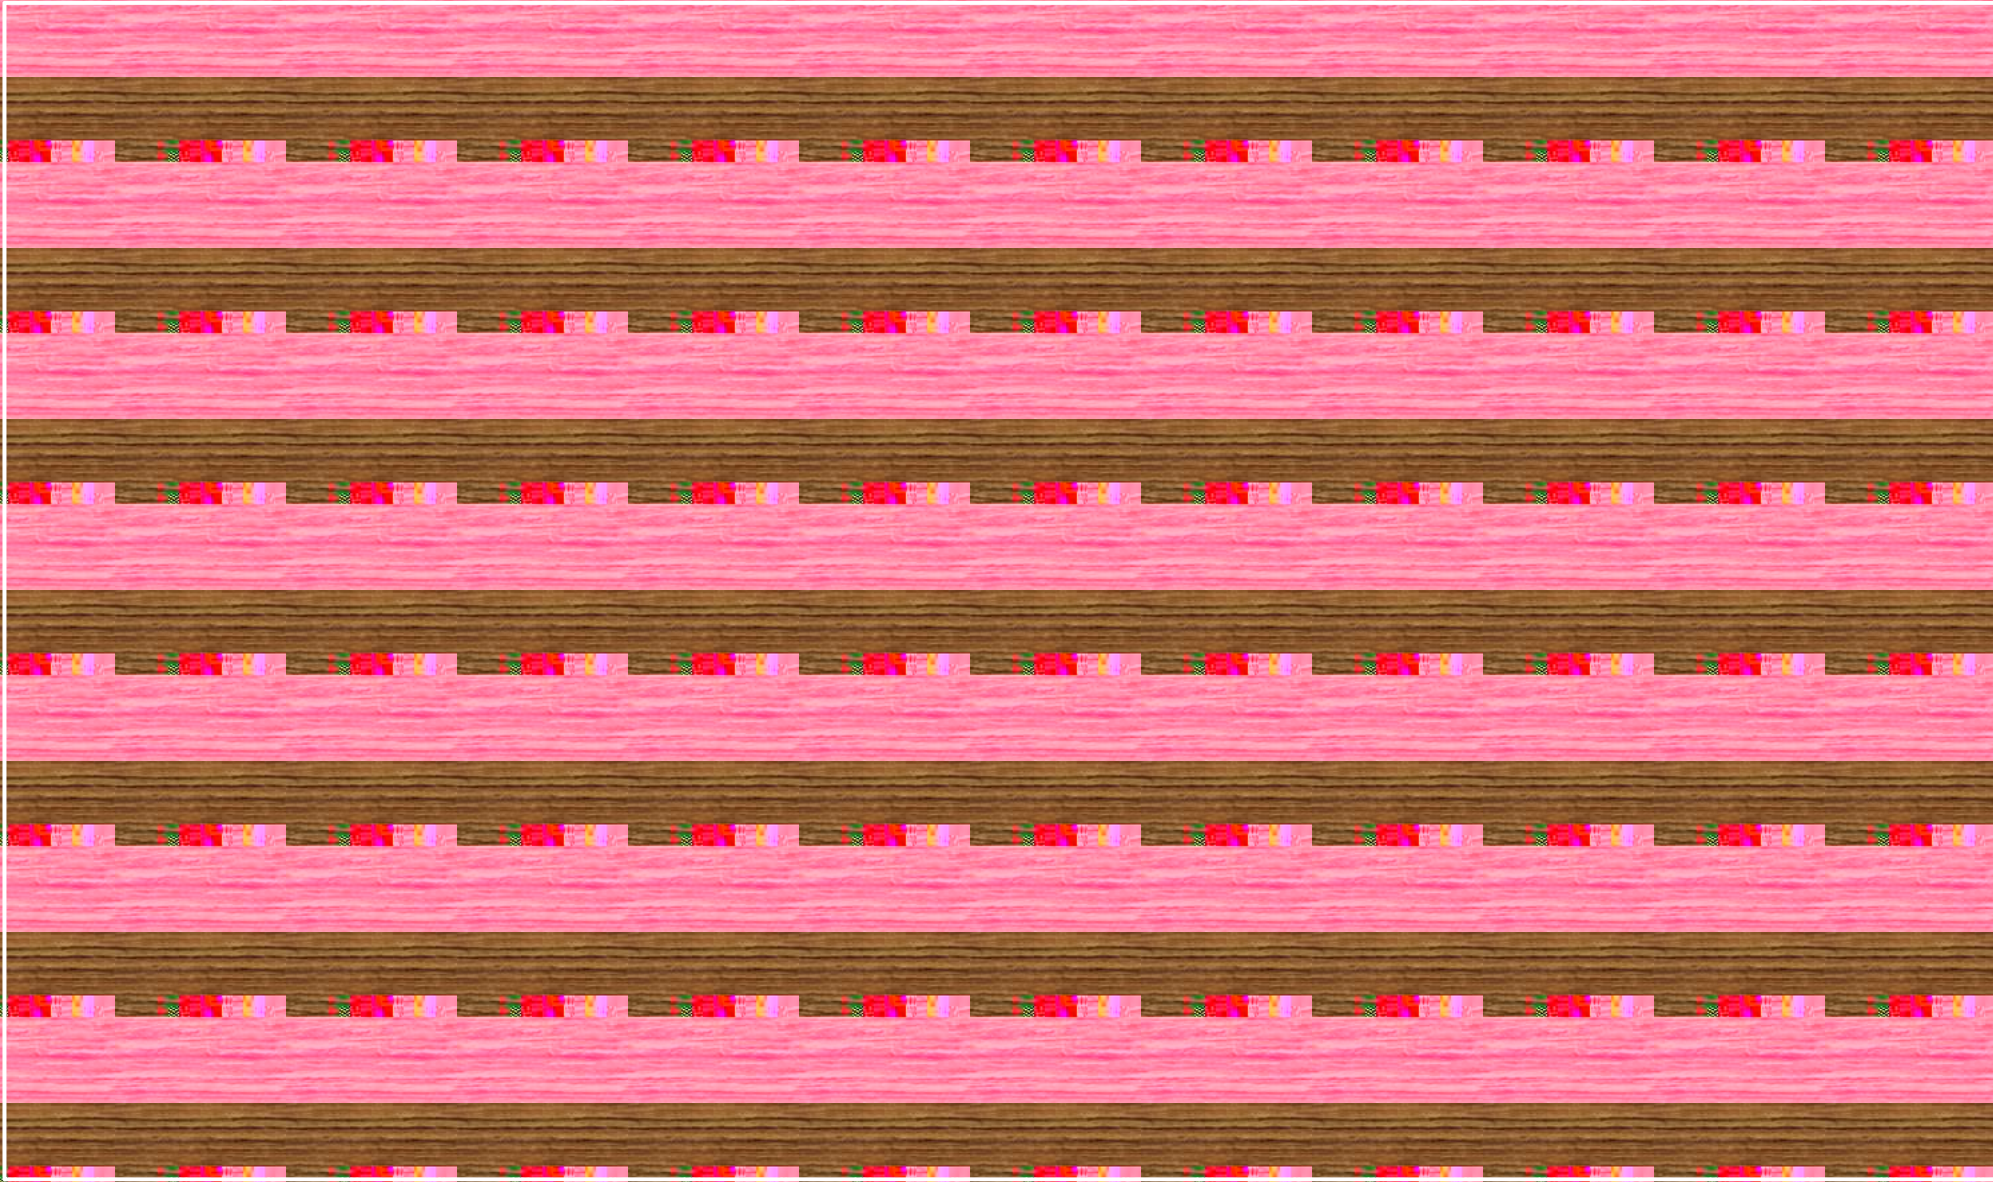



Aerial facing west highlighting the Performing Arts Center and main office.

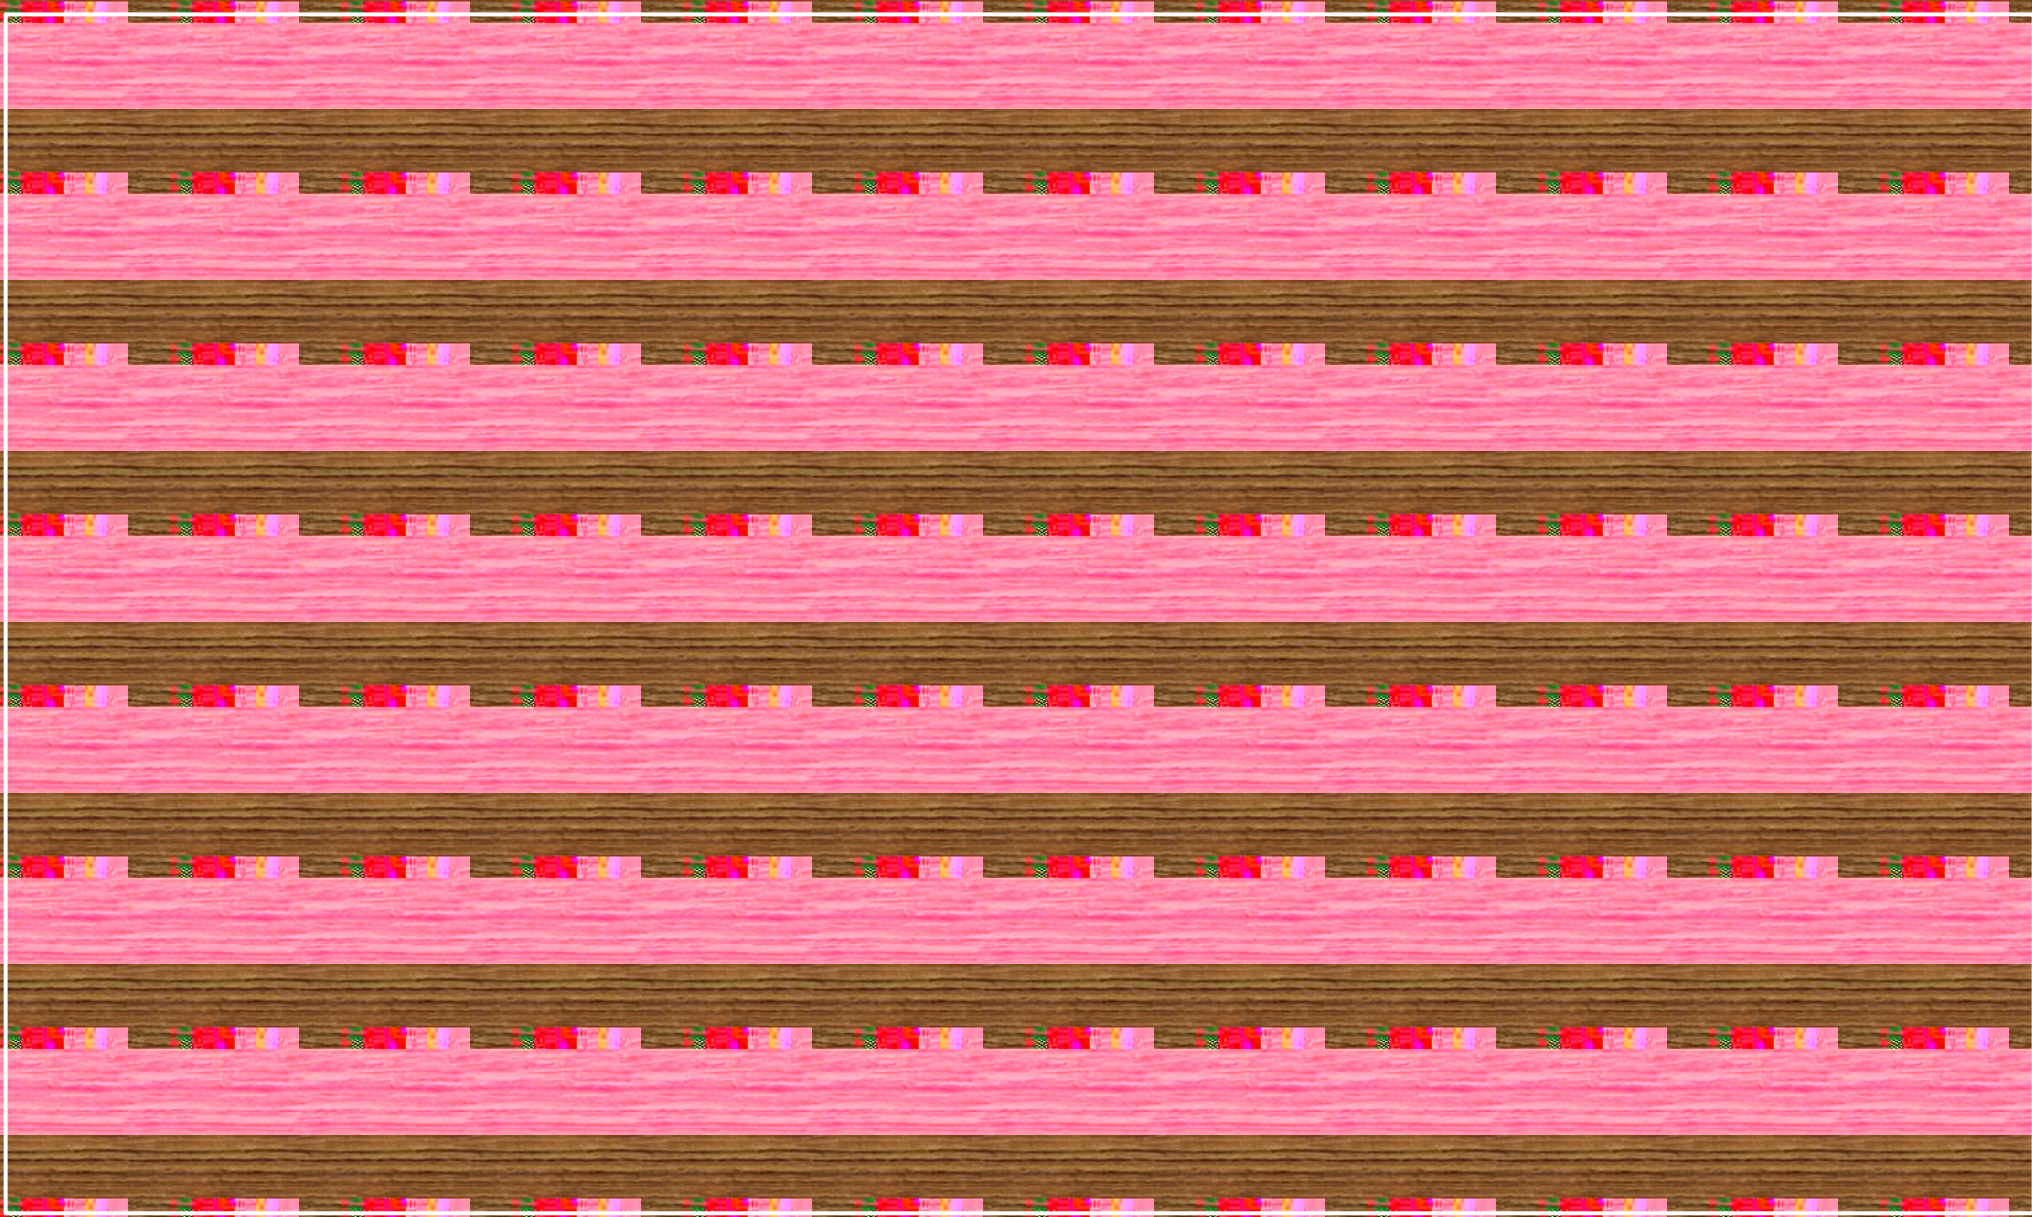



Aerial facing north highlighting the gymnasiums.

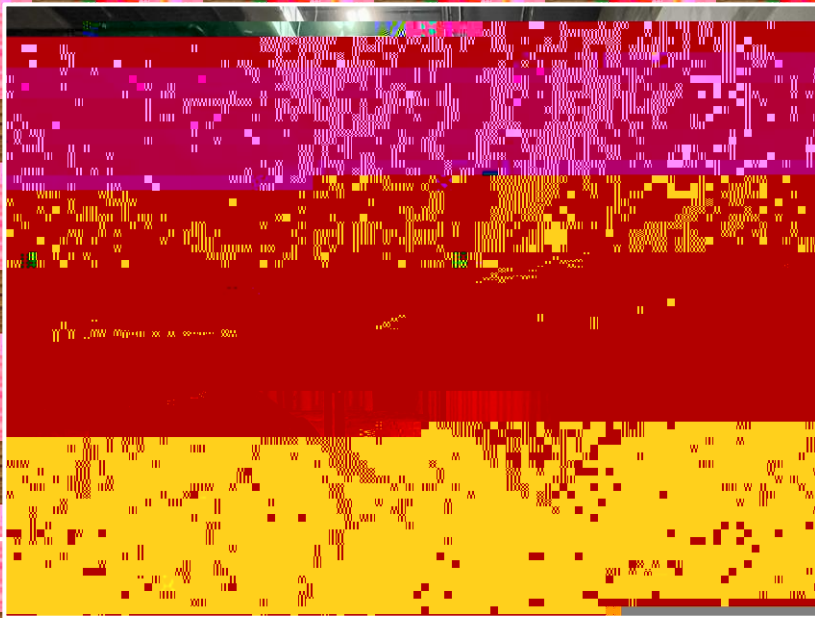



- Ø Percussion walls are being prepped for finish work.
- Ø Entrance to the auditorium vestibule is receiving spray foam insulation. Duct work and electrical are being installed in ceiling.
- Ø ICF walls for the main gymnasium are being prepped. Seating structure has been completed.

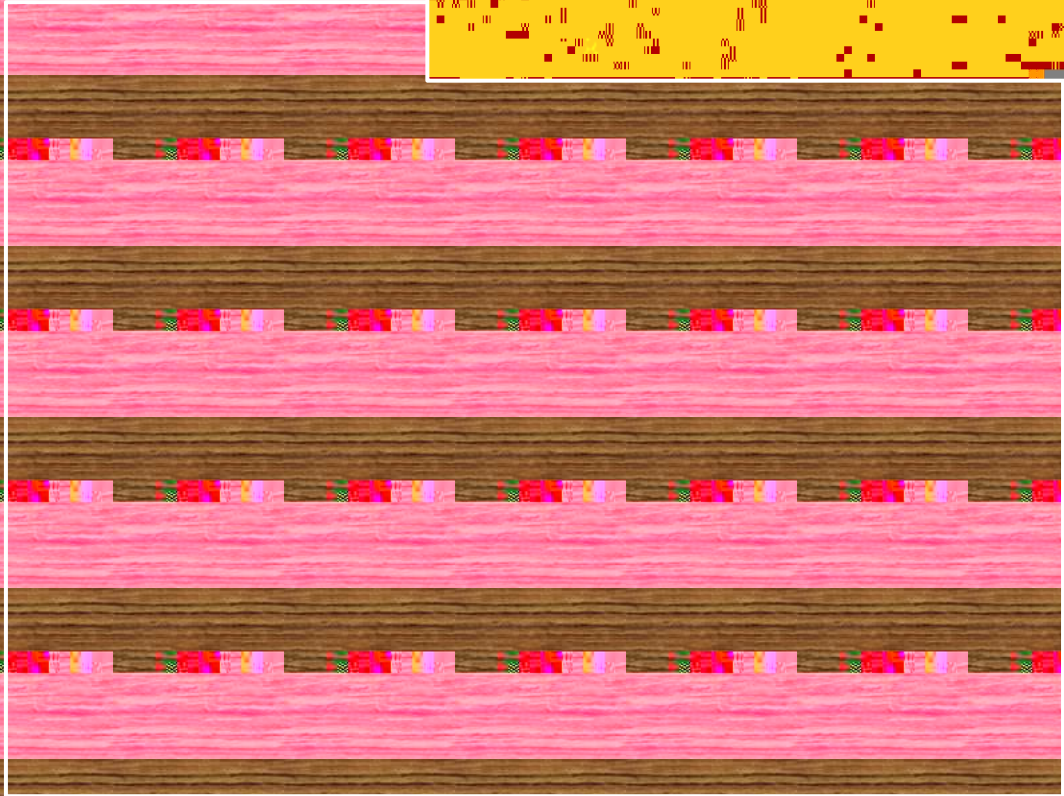

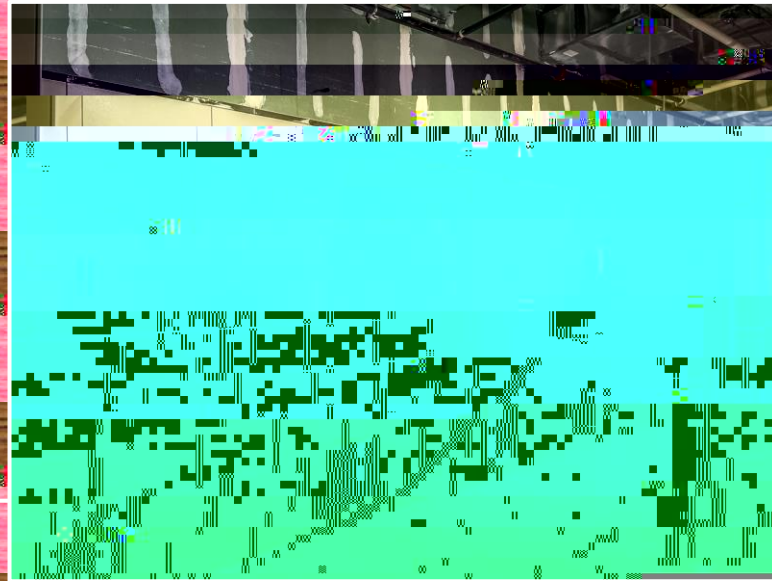

- Ø Interior stone and wall tile installation is complete at the Bistro. Quarry tile flooring is also complete and covered for protection.
- Ø Ceiling grid is being installed in the administration wing. Walls are textured, primed, and first coat of paint is complete.
- Ø Tile is being installed in the restrooms in the academic building. Above ceiling components are being installed in preparation for ceiling grid.

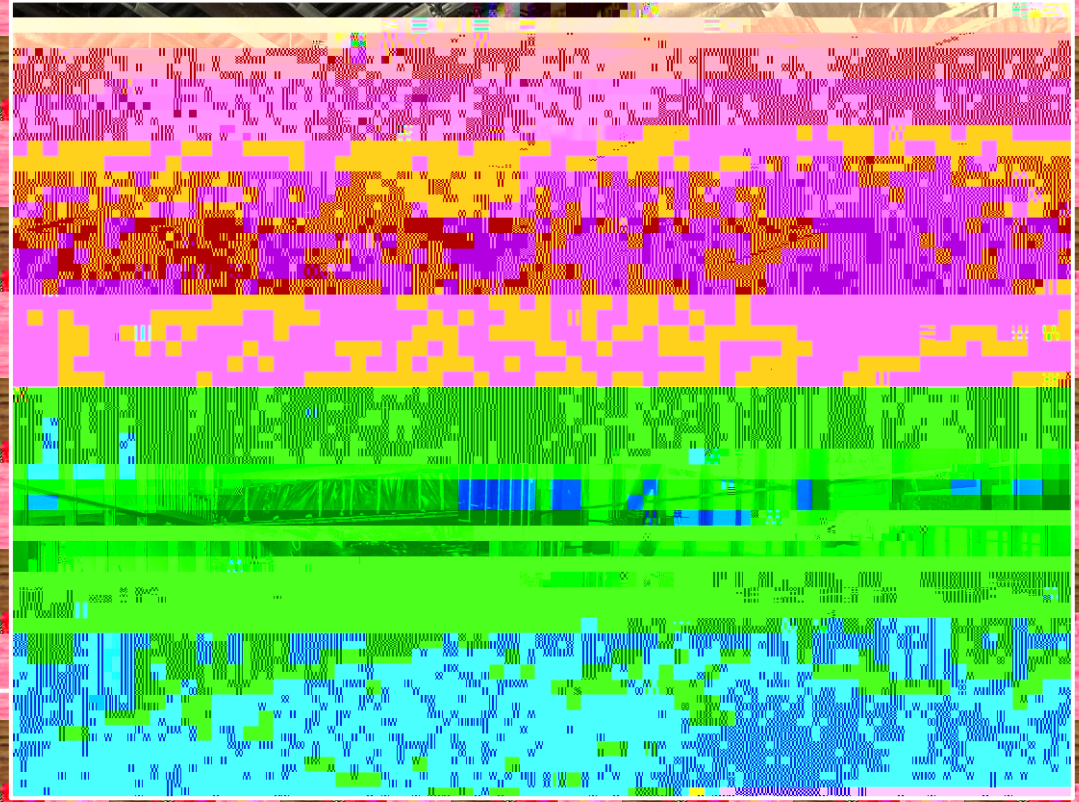

- Ø Interior curtain wall windows are complete at the library.
- Ø Window frames have been installed at the bridge and glass is being installed.
- Ø Cafeteria finishes are progressing. Tile on the back walls, curtain wall windows completed, the ceiling grid and light fixture installation has begun.



- Ø Wall tile at the main kitchen is complete. Duct work and overhead electrical are being installed.
- Ø Corridor tile between cafeteria and auditorium is complete. Above ceiling work is ongoing in preparation for ceiling grid.



- Ø Bleachers at the auxiliary field are being installed. Gravel is in place in preparation for final turf install.
- Ø Baseball field has received gravel for final turf
